


FOUND SMALL RAIL ROAD SPIKE IN MONUMENT
 BOX REMOVED SPIKE AND DUG DOWN 1.5'
 FOUND NO OTHER EVIDENCE SET 3/4" X 24"
 SMOOTH IRON ROD AND 2 1/2" ALUMINUM
 REMON CAP #28414 IN MONUMENT BOX
 IN E MERIDIAN ROAD AT LOCATION OF
 RAIL ROAD SPIKE
 FOUND NAIL AND TAG #25832 EAST SIDE
 24" OAK S25W 77.87
 FOUND NAIL AND TAG #25832 WEST
 SIDE 166" OAK S30E 49.15
 FOUND NAIL AND TAG #18994 SOUTH SIDE
 FENCE POST WEST 31.39
 FOUND NAIL AND TAG #25832 NORTH SIDE
 FENCE POST N85W 31.93
 FOUND NAIL AND TAG #25832 NORTH EAST
 SIDE 10" OAK N60W 30.82
 FOUND NAIL AND TAG #25832 NORTH SIDE
 36" OAK EAST 50.85
 FOUND IRON AXLE EAST 29.76

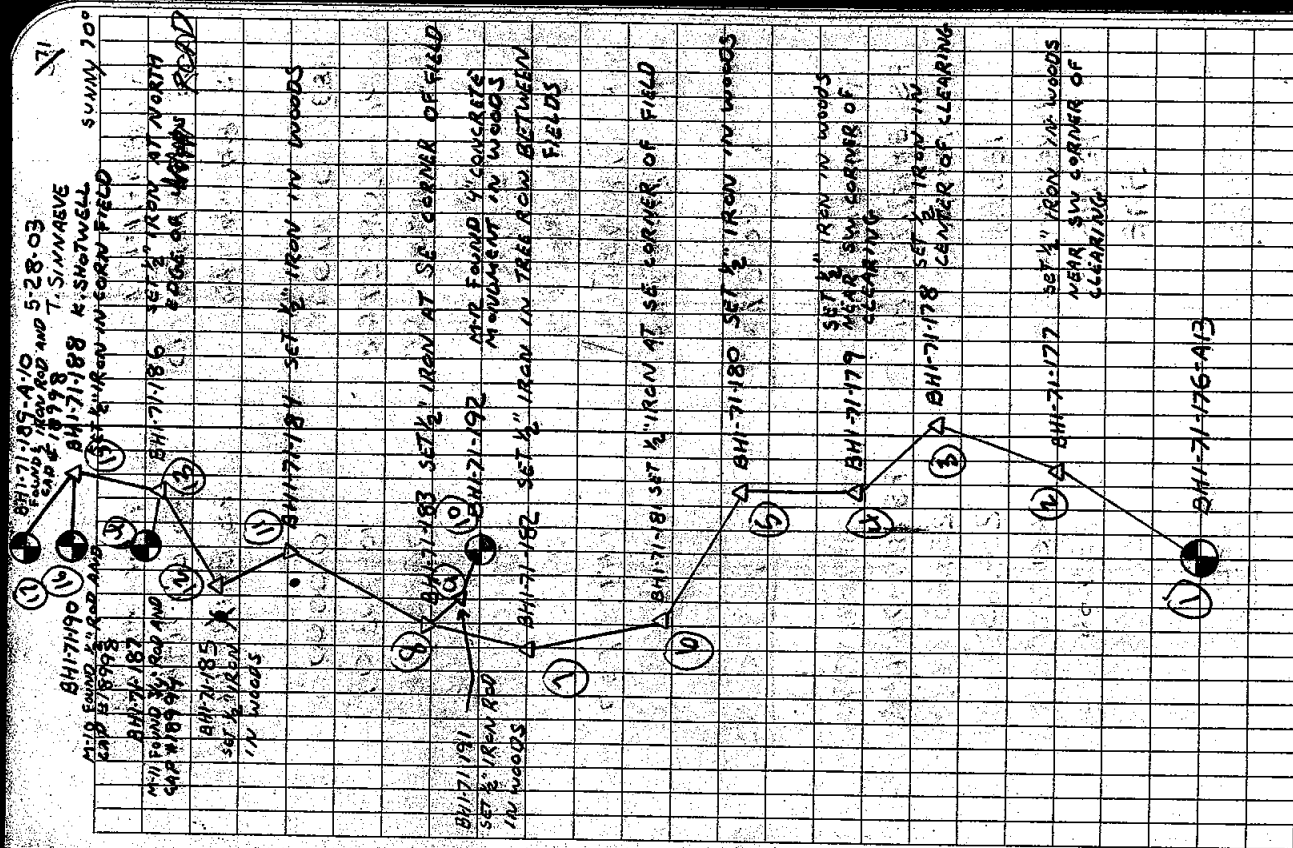

PROJECT: 03-0403
DESCRIPTION: 2003 INGHAM COUNTY REMON
FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

10:42 AM

PAGE 1

TRAV	4	5	N 00°17'00.0" W	289.580	5817.5752	5025.3811
TRAV	5	6	N 21°00'02.0" W	286.330	6084.8862	4922.7670
TRAV	6	7	N 08°43'19.0" W	417.620	6497.6768	4859.4393
TRAV	7	8	N 10°32'56.0" E	280.230	6773.1707	4910.7423
SIDE	8	9	S 75°18'51.0" E	192.600	6724.3430	5097.0501

INSTRUMENT SETUP

Instrument point: 8 6773.1707 4910.7423
Backsight point: 7 6497.6768 4859.4393
Backsight Bearing: S 10°32'56.0" W Distance: 280.230
Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	8	11	N 10°09'46.0" E	853.780	7613.5553	5061.3878
TRAV	11	12	N 14°52'07.0" E	431.930	8031.0229	5172.2225
TRAV	12	13	N 28°23'02.0" E	1305.280	9179.3851	5792.7223
TRAV	13	15	N 10°46'43.0" E	1976.090	11120.6112	6162.2800

INSTRUMENT SETUP

Instrument point: 9 6724.3430 5097.0501
Backsight point: 8 6773.1707 4910.7423
Backsight Bearing: N 75°18'51.0" W Distance: 192.600
Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	9	10	S 75°01'49.0" E	123.670	6692.3979	5216.5231

INSTRUMENT SETUP

Instrument point: 13 9179.3851 5792.7223
Backsight point: 12 8031.0229 5172.2225
Backsight Bearing: S 28°23'02.0" W Distance: 1305.280
Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	13	14	N 52°52'36.0" W	167.150	9280.2656	5659.4473

INSTRUMENT SETUP

Instrument point: 15 11120.6112 6162.2800
Backsight point: 13 9179.3851 5792.7223
Backsight Bearing: S 10°46'43.0" W Distance: 1976.090
Remarks:

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

10:51 AM

PAGE 2

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
SIDE	15	16	N 01°55'18.0" W	760.100	11880.2837	6136.7915
SIDE	15	17	N 04°56'12.0" E	1654.200	12768.6748	6304.6314

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000
 Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	10	N 07°17'26.7" E	1706.193	6692.3979	5216.5231
INV	10	14	N 09°42'44.3" E	2625.498	9280.2656	5659.4473
INV	14	16	N 10°24'11.6" E	2643.473	11880.2837	6136.7915
INV	16	17	N 10°41'54.8" E	904.107	12768.6748	6304.6314

COORDINATE ROTATION-TRANSLATION

Rotation point: 1 5000.0000 5000.0000
 Destination point: 1 5000.0000 5000.0000
 Rotation: 352°49'07.3" Right
 Translation: 0.000 North 0.000 East 0.000 Down

FROM	NORTHING	EASTING	ELEV.	TO	NORTHING	EASTING	ELEV.
1	5000.0000	5000.0000		1	5000.0000	5000.0000	
2	5127.4932	5022.4805		2	5129.3034	5006.3663	
3	5326.8352	5180.9560		3	5346.8926	5138.6790	
4	5527.9987	5026.8131		4	5527.2087	4960.5980	
5	5817.5752	5025.3811		5	5814.3346	4922.9775	
6	6084.8862	4922.7670		6	6066.7211	4787.7520	
7	6497.6768	4859.4393		7	6468.3570	4673.3184	
8	6773.1707	4910.7423		8	6748.1031	4689.7796	
9	6724.3430	5097.0501		9	6722.9487	4880.7299	
10	6692.3979	5216.5231		10	6706.1894	5003.2591	
11	7613.5553	5061.3878		11	7600.7274	4734.1875	
12	8031.0229	5172.2225		12	8028.7756	4791.9654	
13	9179.3851	5792.7223		13	9245.6978	5264.0419	
14	9280.2656	5659.4473		14	9329.1264	5119.2013	
15	11120.6112	6162.2800		15	11217.8943	5388.0293	
16	11880.2837	6136.7915		16	11968.4213	5267.7746	
17	12768.6748	6304.6314		17	12870.8250	5323.2408	

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

10:54 AM

PAGE 3

Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	2	N 02°49'07.3" E	129.460	5129.3034	5006.3663
INV	2	3	N 31°18'11.3" E	254.660	5346.8926	5138.6790
INV	3	4	N 44°38'33.7" W	253.430	5527.2087	4960.5980
INV	4	5	N 07°27'52.7" W	289.580	5814.3346	4922.9775
INV	5	6	N 28°10'54.7" W	286.330	6066.7211	4787.7520
INV	6	7	N 15°54'11.7" W	417.620	6468.3570	4673.3184
INV	7	8	N 03°22'03.3" E	280.230	6748.1031	4689.7796
INV	8	11	N 02°58'53.3" E	853.780	7600.7274	4734.1875
INV	11	12	N 07°41'14.3" E	431.930	8028.7756	4791.9654
INV	12	13	N 21°12'09.3" E	1305.280	9245.6978	5264.0419
INV	13	15	N 03°35'50.3" E	1976.090	11217.8943	5388.0293
INV	15	17	N 02°14'40.7" W	1654.200	12870.8250	5323.2408
INV	17	16	S 03°31'02.1" W	904.107	11968.4213	5267.7746
INV	16	9	S 04°13'12.0" W	5259.733	6722.9487	4880.7299
INV	9	10	S 82°12'41.7" E	123.670	6706.1894	5003.2591
INV	10	1	S 00°06'34.0" W	1706.193	5000.0000	5000.0000
INV	1	10	N 00°06'34.0" E	1706.193	6706.1894	5003.2591
INV	10	14	N 02°31'51.6" E	2625.498	9329.1264	5119.2013
INV	14	16	N 03°13'19.0" E	2643.473	11968.4213	5267.7746
INV	16	17	N 03°31'02.1" E	904.107	12870.8250	5323.2408

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000
 Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	2	02°49'07.3"AR	129.460	5129.3034	5006.3663
INV	2	3	208°29'04.0"AR	254.660	5346.8926	5138.6790
INV	3	4	104°03'15.0"AR	253.430	5527.2087	4960.5980
INV	4	5	217°10'41.0"AR	289.580	5814.3346	4922.9775
INV	5	6	159°16'58.0"AR	286.330	6066.7211	4787.7520
INV	6	7	192°16'43.0"AR	417.620	6468.3570	4673.3184
INV	7	8	199°16'15.0"AR	280.230	6748.1031	4689.7796
INV	8	9	274°08'13.0"AR	192.600	6722.9487	4880.7299
INV	9	10	180°17'02.0"AR	123.670	6706.1894	5003.2591
INV	10	11	65°28'14.2"AR	934.129	7600.7274	4734.1875
INV	11	12	204°25'41.8"AR	431.930	8028.7756	4791.9654
INV	12	8	356°52'28.9"AR	1284.743	6748.1031	4689.7796
INV	8	11	358°25'10.1"AR	853.780	7600.7274	4734.1875

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

11:00 AM

PAGE 4

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	11	12	184°42'21.0"AR	431.930	8028.7756	4791.9654

COORDINATE ROTATION-TRANSLATION

Rotation point: 12 8028.7756 4791.9654
 Destination point: 12 8028.7756 4791.9654
 Rotation: 357°00'00.0" Right
 Translation: 0.000 North 0.000 East 0.000 Down

FROM	NORTHING	EASTING	ELEV.	TO	NORTHING	EASTING	ELEV.
13	9245.6978	5264.0419		13	9268.7367	5199.7061	
14	9329.1264	5119.2013		14	9344.4705	5050.6977	
15	11217.8943	5388.0293		15	11244.7193	5220.3069	
16	11968.4213	5267.7746		16	11987.9241	5060.9374	
17	12870.8250	5323.2408		17	12891.9940	5069.0994	

INSTRUMENT SETUP

Instrument point: 10 6706.1894 5003.2591
 Backsight point: 14 9344.4705 5050.6977
 Backsight Bearing: N 01°01'48.4" E Distance: 2638.707
 Remarks:

INSTRUMENT SETUP

Instrument point: 8 6748.1031 4689.7796
 Backsight point: 8 6748.1031 4689.7796
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	8	11	N 02°58'53.3" E	853.780	7600.7274	4734.1875
INV	11	12	N 07°41'14.3" E	431.930	8028.7756	4791.9654
INV	12	13	190°30'55.0"AR	1305.280	9268.7367	5199.7061

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003
 11:03 AM
 PAGE 5

COORDINATE ROTATION-TRANSLATION

Rotation point: 12 8028.7756 4791.9654
 Destination point: 12 8028.7756 4791.9654
 Rotation: 357°00'00.0" Right
 Translation: 0.000 North 0.000 East 0.000 Down

FROM	NORTHING	EASTING	ELEV.	TO	NORTHING	EASTING	ELEV.
13	9268.7367	5199.7061		13	9288.3768	5134.2528	
14	9344.4705	5050.6977		14	9356.2084	4981.4850	
15	11244.7193	5220.3069		15	11262.7296	5051.4103	
16	11987.9241	5060.9374		16	11996.5751	4853.3630	
17	12891.9940	5069.0994		17	12899.8332	4814.1984	

INSTRUMENT SETUP

Instrument point: 8 6748.1031 4689.7796
 Backsight point: 8 6748.1031 4689.7796
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	8	11	02°58'53.3"AR	853.780	7600.7274	4734.1875
INV	11	12	184°42'21.0"AR	431.930	8028.7756	4791.9654
INV	12	13	187°30'55.0"AR	1305.280	9288.3768	5134.2528

INSTRUMENT SETUP

Instrument point: 11 7600.7274 4734.1875
 Backsight point: 8 6748.1031 4689.7796
 Backsight Bearing: S 02°58'53.3" W Distance: 853.780
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	11	12	181°42'21.0"AR	431.930	8031.2129	4769.4839
TRAV	12	13	193°30'55.0"AR	1305.280	9271.1739	5177.2247
TRAV	13	15	162°23'41.0"AR	1976.090	11247.1565	5197.8254

INSTRUMENT SETUP

Instrument point: 13 9271.1739 5177.2247
 Backsight point: 12 8031.2129 4769.4839
 Backsight Bearing: S 18°12'09.3" W Distance: 1305.280
 Remarks:

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

11:06 AM

PAGE 6

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	13	14	98°44'22.0"AR	167.150	9346.9077	5028.2162

INSTRUMENT SETUP

Instrument point: 15 11247.1565 5197.8254
 Backsight point: 13 9271.1739 5177.2247
 Backsight Bearing: S 00°35'50.3" W Distance: 1976.090
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
SIDE	15	16	167°17'59.0"AR	760.100	11990.3613	5038.4559
SIDE	15	17	174°09'29.0"AR	1654.200	12894.4312	5046.6179

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000
 Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	2	02°49'07.3"AR	129.460	5129.3034	5006.3663
INV	2	3	208°29'04.0"AR	254.660	5346.8926	5138.6790
INV	3	4	104°03'15.0"AR	253.430	5527.2087	4960.5980
INV	4	5	217°10'41.0"AR	289.580	5814.3346	4922.9775
INV	5	6	159°16'58.0"AR	286.330	6066.7211	4787.7520
INV	6	7	192°16'43.0"AR	417.620	6468.3570	4673.3184
INV	7	8	199°16'15.0"AR	280.230	6748.1031	4689.7796
INV	8	11	179°36'50.0"AR	853.780	7600.7274	4734.1875
INV	11	12	181°42'21.0"AR	431.930	8031.2129	4769.4839
INV	12	13	193°30'55.0"AR	1305.280	9271.1739	5177.2247
INV	13	15	162°23'41.0"AR	1976.090	11247.1565	5197.8254

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000
 Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	10	00°06'34.0"AR	1706.193	6706.1894	5003.2591
INV	10	14	180°25'55.3"AR	2640.836	9346.9077	5028.2162

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

11:08 AM

PAGE 7

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	14	16	179°40'49.7"AR	2643.473	11990.3613	5038.4559
INV	16	17	180°17'43.1"AR	904.107	12894.4312	5046.6179
INV	17	1	S 00°20'18.0" W	7894.569	5000.0000	5000.0000
INV	1	10	N 00°06'34.0" E	1706.193	6706.1894	5003.2591
INV	10	14	N 00°32'29.3" E	2640.836	9346.9077	5028.2162
INV	14	16	N 00°13'19.0" E	2643.473	11990.3613	5038.4559
INV	16	17	N 00°31'02.1" E	904.107	12894.4312	5046.6179
INV	17	1	S 00°20'18.0" W	7894.569	5000.0000	5000.0000

INSTRUMENT SETUP

Instrument point: 10 6706.1894 5003.2591
 Backsight point: 10 6706.1894 5003.2591
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	10	20	N 00°32'29.3" E	923.790	7629.9382	5011.9893

INSTRUMENT SETUP

Instrument point: 14 9346.9077 5028.2162
 Backsight point: 16 11990.3613 5038.4559
 Backsight Bearing: N 00°13'19.0" E Distance: 2643.473
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
TRAV	14	21	N 00°13'19.0" E	912.930	10259.8309	5031.7525

INSTRUMENT SETUP

Instrument point: 1 5000.0000 5000.0000
 Backsight point: 1 5000.0000 5000.0000
 Backsight Bearing: N 00°00'00.0" E Distance: 0.000
 Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	10	N 00°06'34.0" E	1706.193	6706.1894	5003.2591
INV	10	20	N 00°32'29.3" E	923.790	7629.9382	5011.9893
INV	20	14	N 00°32'29.3" E	1717.046	9346.9077	5028.2162
INV	14	21	N 00°13'19.0" E	912.930	10259.8309	5031.7525
INV	21	16	N 00°13'19.0" E	1730.543	11990.3613	5038.4559
INV	16	17	N 00°31'02.1" E	904.107	12894.4312	5046.6179

PROJECT: 03-0403
DESCRIPTION: 2003 INGHAM COUNTY REMON
FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

11:19 AM

PAGE 8

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	17	17	N 00°00'00.0" E	0.000	12894.4312	5046.6179
INV	17	16	S 00°31'02.1" W	904.107	11990.3613	5038.4559
INV	16	21	S 00°13'19.0" W	1730.543	10259.8309	5031.7525
INV	21	14	S 00°13'19.0" W	912.930	9346.9077	5028.2162
INV	14	20	S 00°32'29.3" W	1717.046	7629.9382	5011.9893
INV	20	10	S 00°32'29.3" W	923.790	6706.1894	5003.2591
INV	10	1	S 00°06'34.0" W	1706.193	5000.0000	5000.0000

PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT


Monday, June 30, 2003

11:30 AM


PAGE 9

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	2	N 02°49'07.3" E	129.460	5129.3034	5006.3663
INV	2	3	N 31°18'11.3" E	254.660	5346.8926	5138.6790
INV	3	4	N 44°38'33.7" W	253.430	5527.2087	4960.5980
INV	4	5	N 07°27'52.7" W	289.580	5814.3346	4922.9775
INV	5	6	N 28°10'54.7" W	286.330	6066.7211	4787.7520
INV	6	7	N 15°54'11.7" W	417.620	6468.3570	4673.3184
INV	7	8	N 03°22'03.3" E	280.230	6748.1031	4689.7796
INV	8	11	N 02°58'53.3" E	853.780	7600.7274	4734.1875
INV	11	12	N 04°41'14.3" E	431.930	8031.2129	4769.4839
INV	12	13	N 18°12'09.3" E	1305.280	9271.1739	5177.2247
INV	13	15	N 00°35'50.3" E	1976.090	11247.1565	5197.8254
INV	15	11	S 07°14'46.3" W	3675.786	7600.7274	4734.1875
INV	11	20	N 83°59'50.7" E	279.333	7629.9382	5011.9893
INV	20	13	N 05°44'56.5" E	1649.532	9271.1739	5177.2247
INV	13	21	N 08°22'13.8" W	999.302	10259.8309	5031.7525
INV	21	15	N 09°32'53.0" E	1001.195	11247.1565	5197.8254
INV	15	16	N 12°06'10.7" W	760.100	11990.3613	5038.4559

TYPE	POINT	NORTHING	EASTING	ELEV.	DESCRIPTION
LIST	1	5000.0000	5000.0000		
LIST	2	5129.3034	5006.3663		
LIST	3	5346.8926	5138.6790		
LIST	4	5527.2087	4960.5980		
LIST	5	5814.3346	4922.9775		
LIST	6	6066.7211	4787.7520		
LIST	7	6468.3570	4673.3184		
LIST	8	6748.1031	4689.7796		
LIST	9	6722.9487	4880.7299		
LIST	10	6706.1894	5003.2591		
LIST	11	7600.7274	4734.1875		
LIST	12	8031.2129	4769.4839		
LIST	13	9271.1739	5177.2247		
LIST	14	9346.9077	5028.2162		
LIST	15	11247.1565	5197.8254		
LIST	16	11990.3613	5038.4559		
LIST	17	12894.4312	5046.6179		
LIST	20	7629.9382	5011.9893		
LIST	21	10259.8309	5031.7525		



1:1000



PROJECT: 03-0403
 DESCRIPTION: 2003 INGHAM COUNTY REMON
 FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
 UNITS: U.S. SURVEY FOOT

Monday, June 30, 2003

11:30 AM

PAGE 9

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	1	2	N 02°49'07.3" E	129.460	5129.3034	5006.3663
INV	2	3	N 31°18'11.3" E	254.660	5346.8926	5138.6790
INV	3	4	N 44°38'33.7" W	253.430	5527.2087	4960.5980
INV	4	5	N 07°27'52.7" W	289.580	5814.3346	4922.9775
INV	5	6	N 28°10'54.7" W	286.330	6066.7211	4787.7520
INV	6	7	N 15°54'11.7" W	417.620	6468.3570	4673.3184
INV	7	8	N 03°22'03.3" E	280.230	6748.1031	4689.7796
INV	8	11	N 02°58'53.3" E	853.780	7600.7274	4734.1875
INV	11	12	N 04°41'14.3" E	431.930	8031.2129	4769.4839
INV	12	13	N 18°12'09.3" E	1305.280	9271.1739	5177.2247
INV	13	15	N 00°35'50.3" E	1976.090	11247.1565	5197.8254
INV	15	11	S 07°14'46.3" W	3675.786	7600.7274	4734.1875
INV	11	20	N 83°59'50.7" E	279.333	7629.9382	5011.9893
INV	20	13	N 05°44'56.5" E	1649.532	9271.1739	5177.2247
INV	13	21	N 08°22'13.8" W	999.302	10259.8309	5031.7525
INV	21	15	N 09°32'53.0" E	1001.195	11247.1565	5197.8254
INV	15	16	N 12°06'10.7" W	760.100	11990.3613	5038.4559

TYPE	POINT	NORTHING	EASTING	ELEV.	DESCRIPTION
LIST	1	5000.0000	5000.0000		
LIST	2	5129.3034	5006.3663		
LIST	3	5346.8926	5138.6790		
LIST	4	5527.2087	4960.5980		
LIST	5	5814.3346	4922.9775		
LIST	6	6066.7211	4787.7520		
LIST	7	6468.3570	4673.3184		
LIST	8	6748.1031	4689.7796		
LIST	9	6722.9487	4880.7299		
LIST	10	6706.1894	5003.2591		
LIST	11	7600.7274	4734.1875		
LIST	12	8031.2129	4769.4839		
LIST	13	9271.1739	5177.2247		
LIST	14	9346.9077	5028.2162		
LIST	15	11247.1565	5197.8254		
LIST	16	11990.3613	5038.4559		
LIST	17	12894.4312	5046.6179		
LIST	20	7629.9382	5011.9893		
LIST	21	10259.8309	5031.7525		

PROJECT: 03-0403
DESCRIPTION: 2003 INGHAM COUNTY REMON
FILE: S:\PROJECTS\2003\03-0403\03-0403.CGO
UNITS: U.S. SURVEY FOOT

Thursday, July 31, 2003

9:15 AM

PAGE 1

INSTRUMENT SETUP

Instrument point: 17 12894.4312 5046.6179
Backsight point: 16 11990.3613 5038.4559
Backsight Bearing: S 00°31'02.1" W Distance: 904.107
Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	17	16	S 00°31'02.1" W	904.107	11990.3613	5038.4559
INV	16	21	S 00°13'19.0" W	1730.543	10259.8309	5031.7525
INV	21	124			-	-
INV	124	20			-	-
INV	20	10	S 00°32'29.3" W	923.790	6706.1894	5003.2591
INV	10	1	S 00°06'34.0" W	1706.193	5000.0000	5000.0000


INSTRUMENT SETUP

Instrument point: 17 12894.4312 5046.6179
Backsight point: 17 12894.4312 5046.6179
Backsight Bearing: N 00°00'00.0" E Distance: 0.000
Remarks:

TYPE	FROM	TO	DIRECTION	DISTANCE	NORTHING	EASTING
INV	17	16	S 00°31'02.1" W	904.107	11990.3613	5038.4559
INV	16	21	S 00°13'19.0" W	1730.543	10259.8309	5031.7525
INV	21	14	S 00°13'19.0" W	912.930	9346.9077	5028.2162
INV	14	20	S 00°32'29.3" W	1717.046	7629.9382	5011.9893
INV	20	10	S 00°32'29.3" W	923.790	6706.1894	5003.2591
INV	10	1	S 00°06'34.0" W	1706.193	5000.0000	5000.0000

LESLIE TWP TIN, R/W

SECTION 36 SECTION 25

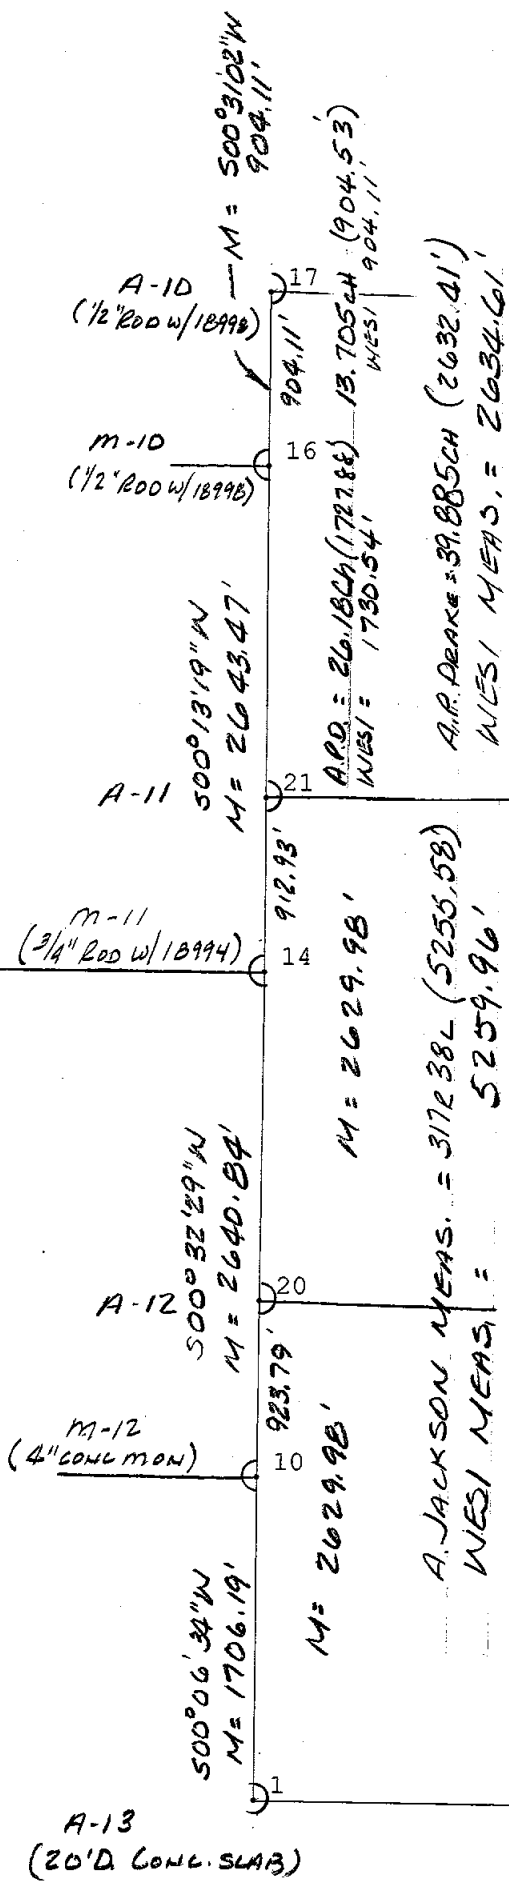

SECTION 30 SECTION 31

BUNKER HILL TWP TIN, R/W




2003 5 28



A-13 Bunkerhill



A-13 BUNGEHIL

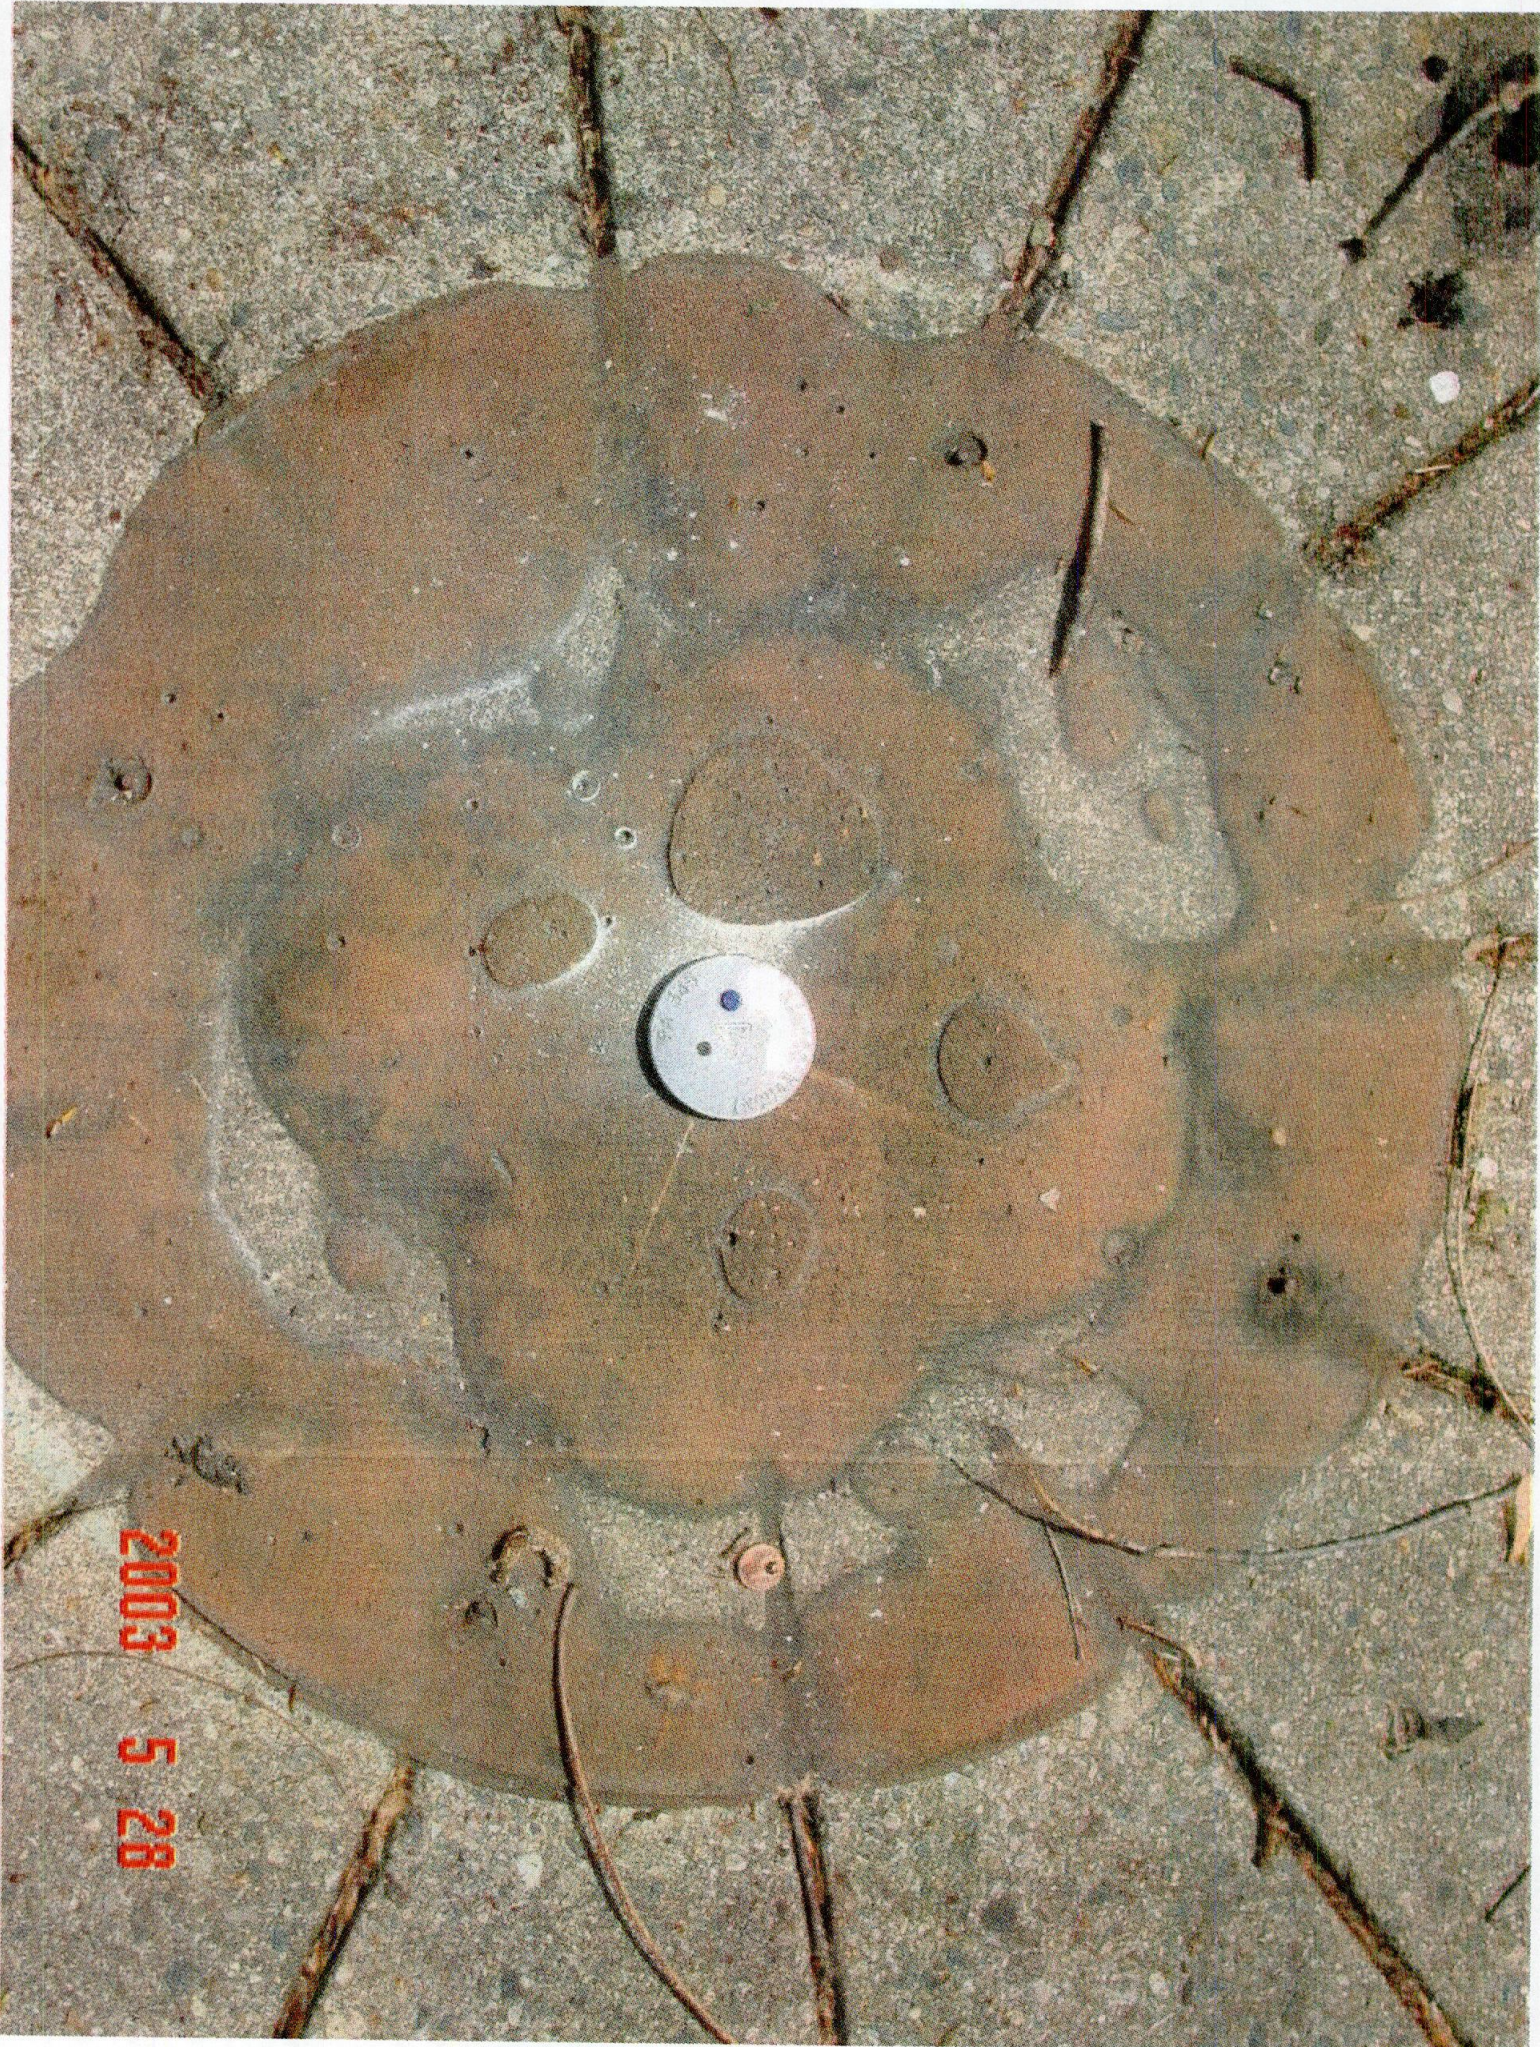

2003 5 28

A-13 BUKERHILL



2003 5 28

A-13 Bunker

